





PROPOSED SEWER FLOW AND CAPACITY
(NOT TO SCALE)

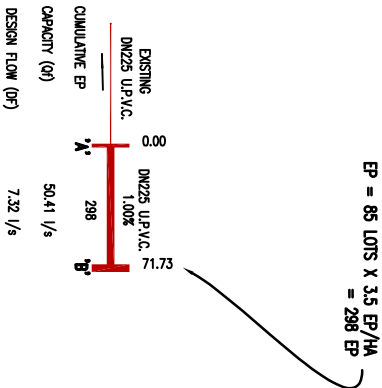

FLOW DIAGRAM – LINE 1
(NOT TO SCALE)

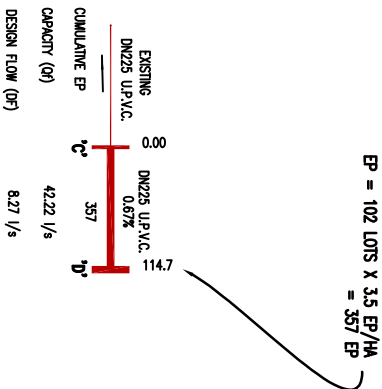

FLOW DIAGRAM – LINE 2
(NOT TO SCALE)

SEWERAGE FLOW SCHEDULE (SUMMARY) : Updated Jan 2016													
Compiled by: P Patel		Date: 29.11.22											
Checked by: F Jaehne		Date: 29.11.22											
Plan No.	EN303433	Location: 421 Cobbitty Rd Cobbitty		JOB No. (SWC use) 00-Jan-90									
e-Developer No	CASE201352	Description: Sewer extension - L1		0									
SUMMARY													
SECTION	CHAINAGE	TOTAL AREA	TOTAL Grav	TOTAL Grav + Pump	PIPE SIZE (DN)	PIPE SIZE (ID)	PIPE GRADE	DESIGN FLOW (QF)	QF (Capacity)	Actual	SELF CLEANSING	SLIME CONTROL	Capacity
A-B	0+1173 (L1)	3.75	286	286	225	233.6	1	7.32	50.41	2.44	Self Cleansing OK	NA	Deficit OK
SEWERAGE FLOW SCHEDULE (SUMMARY) : Updated Jan 2016													
Compiled by: P Patel		Date: 29.11.22											
Checked by: F Jaehne		Date: 29.11.22											
Plan No.	EN303433	Location: 421 Cobbitty Rd Cobbitty		JOB No. (SWC use) 00-Jan-90									
e-Developer No	CASE201352	Description: Sewer extension - L2		0									
SUMMARY													
SECTION	CHAINAGE	TOTAL AREA	TOTAL Grav	TOTAL Grav + Pump	PIPE SIZE (DN)	PIPE SIZE (ID)	PIPE GRADE	DESIGN FLOW (QF)	QF (Capacity)	Actual	SELF CLEANSING	SLIME CONTROL	Capacity
C-D	0+1147 (L2)	3.82	357	357	225	233.6	0.67	8.27	41.22	2.76	Self Cleansing OK	NA	Deficit OK

WORK AS CONSTRUCTED CERTIFICATION				SYDNEY WATER CORPORATION			
DEVELOPER		WATER		Case No.	201349WW	SHT	3 OF 3 SHTS.
W.S.C.		WATER					
CONSTRUCTOR		WATER					
COMPLETED		WATER					
W.A.C. PREPARED		WATER					
DESIGNER		WATER					
I CERTIFY THAT THE WORKS HAVE BEEN CONSTRUCTED IN ACCORDANCE WITH THE WORK AS CONSTRUCTED DRAWINGS				FOR DETAILS OF SERVICES SEE SHEET 1			
